

# Agave Release Plan



## [Document History](#)

<b>Version</b>	<b>Date</b>	<b>Author</b>	<b>Description</b>
0.1	24 July 2006	Frank Bohac	initial Version

## Mission

This document contains a description of the functionality sequencing for upcoming releases of the Agave application. This sequencing is to be used as input to detailed project planning for each release. Note: as releases are implemented, this sequencing is subject to change.

## Functionality Status

Current status of each Agave Functional Group is shown below (see chart of following page).


Function Group	Complete	Remaining
Core Services	<ul style="list-style-type: none"> <li>○ Update Manager</li> <li>○ Navigation</li> <li>○ Messaging</li> <li>○ Utilities</li> <li>○ Audit</li> </ul>	<ul style="list-style-type: none"> <li>○ Tracing</li> <li>○ Rules Engine</li> </ul>
FG1 – Case Management	<ul style="list-style-type: none"> <li>○ Case Initiation</li> <li>○ Case Maintenance</li> </ul>	<ul style="list-style-type: none"> <li>○ Judge</li> <li>○ Attorney</li> <li>○ Courtroom processing</li> <li>○ Arbitration</li> <li>○ Judicial Performance Review</li> <li>○ Dispo &amp; Sentencing</li> </ul>
FG2 – Document Management	<ul style="list-style-type: none"> <li>○ Imaging</li> <li>○ Docketing</li> <li>○ Retrieval</li> </ul>	<ul style="list-style-type: none"> <li>○ Minute Entry</li> </ul>
FG3 - Financial	<ul style="list-style-type: none"> <li>○ Cash Drawer Processing</li> <li>○ Receipting (Criminal/non-Criminal)</li> </ul>	<ul style="list-style-type: none"> <li>○ Disbursement</li> <li>○ Accruals</li> <li>○ Arrearages</li> <li>○ Bank reconciliation</li> <li>○ Check processing</li> <li>○ Bond Management</li> <li>○ General Ledger</li> </ul>
FG4 - Admin	<ul style="list-style-type: none"> <li>○ Code tables</li> <li>○ Security</li> </ul>	<ul style="list-style-type: none"> <li>○ Code tables for new functionality</li> </ul>
FG5 – Stats and Reporting	<ul style="list-style-type: none"> <li>○ Case Initiation</li> </ul>	<ul style="list-style-type: none"> <li>○ Case/Calendar</li> <li>○ Compliance Monitoring</li> </ul>
FG6 - Calendaring		<ul style="list-style-type: none"> <li>○ Scheduling</li> <li>○ Calendar</li> <li>○ Resource Schedules</li> </ul>
SOAP/Interfaces	<ul style="list-style-type: none"> <li>○ PCAO feed</li> <li>○ Lexus/Nexus</li> <li>○ Blueback</li> <li>○ SMEEDLink</li> </ul>	<ul style="list-style-type: none"> <li>○ Distribution Engine</li> <li>○ Subscription Services</li> </ul>
User Interface	<ul style="list-style-type: none"> <li>○ Thick Client (Agave)</li> <li>○ Thin Client (Agave Web)</li> </ul>	

## Functionality Status

Other Remaining:

- Conciliation Court
- Probate
- e-signature
- e-filing

# Agave Functional Groups

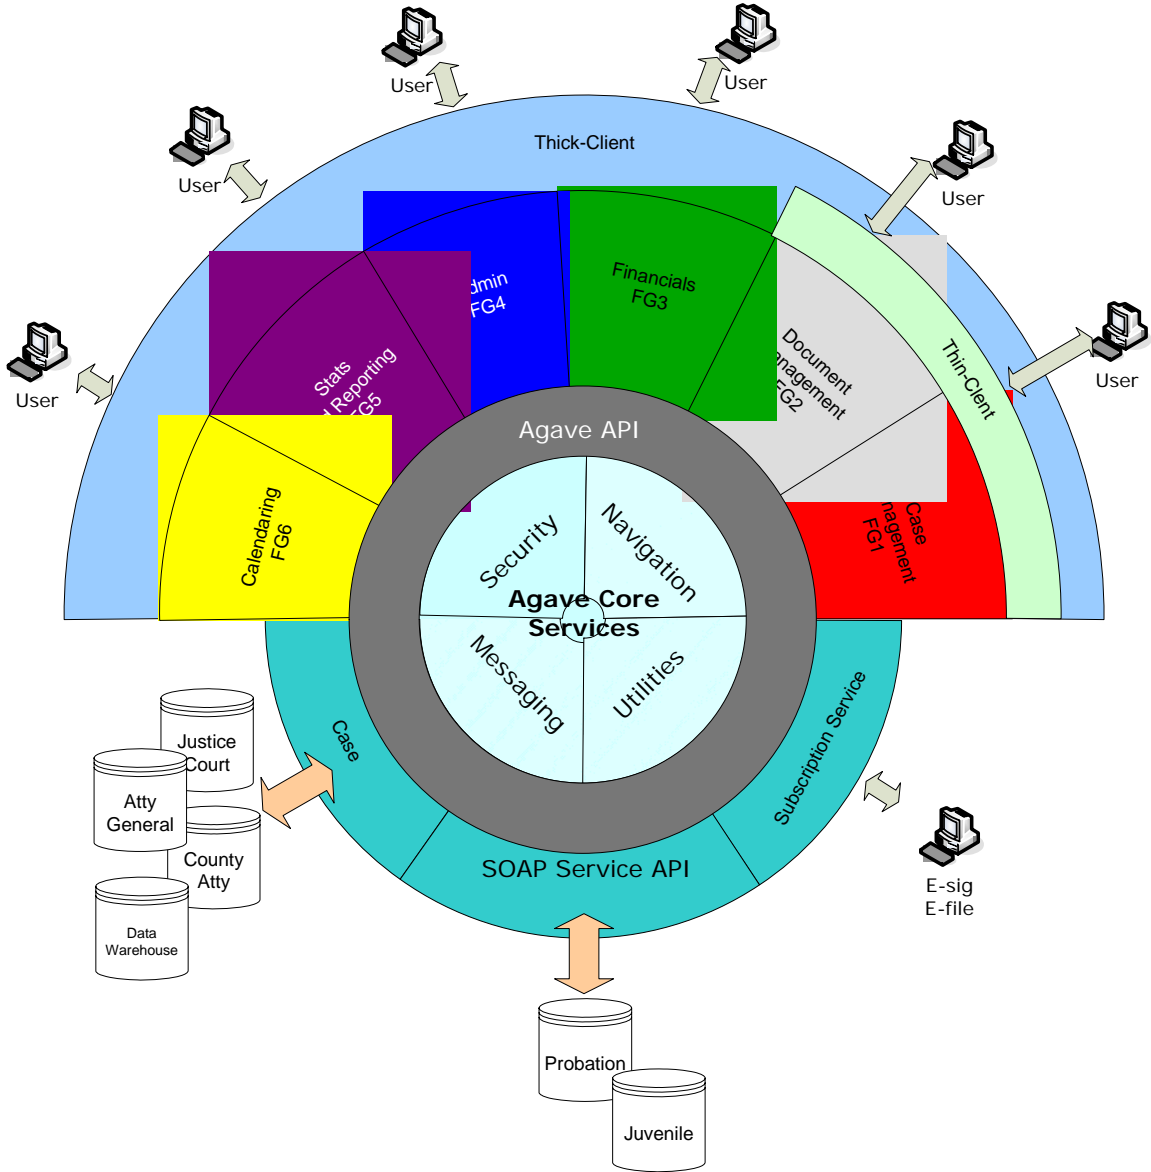

## Release Grouping

### I. Maintenance Release

- a. Re-architect for Visible best practices
- b. CORE Tracing
- c. SQL Server 2005

### II. Rules Engine

- a. Implement Rules Engine
- b. Implement Rules Admin UI
- c. Illogic checks
- d. Redo Caption
- e. Redo Judge Assignment
- f. Redo permissions (?)

### III. Finance

- a. Remainder of Finance

### IV. CACTIS Replacement

- a. FG6 - Calendar
- b. Remainder of FG1 - Case Management (excluding Probate bench)
- c. FG5 – Stats and Reporting (for Calendar/Case Management)
- d. Base Workflows via Rules Engine

### V. Rules Support and Workflow Implementation

- a. via in-house analysis/support

### VI. Courtroom Processing

- a. Minute Entry
- b. Interpreters Program
- c. Courtroom Clerk scheduling
- d. FG5 – Stats and Reporting (for Courtroom processing)

### VII. Distribution Engine

- a. Subscription Services
- b. Alerts
- c. Dispositions
- d. Other external data exchanges

### VIII. Other

- a. Conciliation Court
- b. Probate
- c. e-signature
- d. e-filing

## Release Sequencing

